STATE OF NORTH DAKOTA

BOARD OF WATER WELL CONTRACTORS

900 E. BOULEVARD • BISMARCK, NORTH DAKOTA 58501

WELL DRILLER'S REPORT

State law requires that this report be filed with the State Board of Water Well Contractors within 30 days after completion or abandonment of the well.

1. WELL OWNER

Name: T.P. Memorial Park

Address: Watford City, N.D.

2. WELL LOCATION

Sketch map location must agree with written location.

NORTH

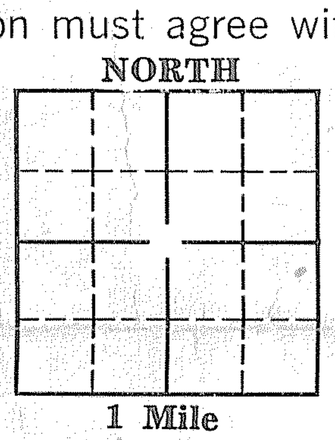

1 Mile

County: McKenzie

NW ¼ NW ¼ SE ¼ Sec. 4 Twp. 147 N. Rg. 99 W.

3. PROPOSED USE

☐ Domestic ☐ Irrigation ☐ Industrial

☒ Stock ☐ Municipal ☐ Test Hole

4. METHOD DRILLED

☒ Cable ☐ Reverse Rotary ☒ Bored

☐ Forward Rotary ☐ Jetted ☐ Other

If other, specify

5. WATER QUALITY

Was a water sample collected for chemical analysis?

☐ Yes ☐ No

If so, to what laboratory was it sent

6. WELL CONSTRUCTION

Diameter of hole 7 inches. Depth 40 feet.

Casing: ☐ Steel ☒ Plastic ☐ Concrete

☐ Threaded ☐ Welded ☐ Other

If other, specify

Pipe Weight:	Diameter:	From:	To:
220 lb/ft.	4 inches	0 feet	40 feet
lb/ft.	inches	feet	feet
lb/ft.	inches	feet	feet
lb/ft.	inches	feet	feet

Was perforated pipe used? ☒ Yes ☐ No

Length of pipe perforated Bottom 15 ft. feet

Was casing left open end? ☒ Yes ☐ No

Was a well screened installed? ☐ Yes ☒ No

Material Diameter inches
(stainless steel, bronze, etc.)

Slot size set from feet to feet

Slot size set from feet to feet

Slot size set from feet to feet

Slot size set from feet to feet

Was a packer or seal used? ☐ Yes ☒ No

If so, what material

Type of well: Straight screen ☐ Gravel packed ☒

Was the well grouted? Yes ☐ No ☐

To what depth? 5' to 15' feet

Material used in grouting mud

Well head completion: Pitless adapter

12" above grade ✓ Other

If other, specify

Was well disinfected upon completion? ☒ Yes ☐ No

7. WATER LEVEL

Static water level 21 feet below land surface

If flowing: closed-in pressure psi

GPM flow through inch pipe

Controlled by: ☐ Valve ☐ Reducers ☐ Other

If other, specify

8. WELL TEST DATA

☐ Pump ☐ Bailer ☐ Other

Pumping level below land surface:

ft. after hrs. pumping gpm

ft. after hrs. pumping gpm

ft. after hrs. pumping gpm

9. WELL LOG

Formation	Depth (ft.) From	Depth (ft.) To
Sandy topsoil	0	3
fine soft dry sand	3	16
clay	16	18
soft brown sand	18	22
coarse grey sand	22	35
rock scale	35	36
coarse beyond	36	
Sand caving from 30 ft up		
had to keep tube overload		
to finish well.		

(Use separate sheet if necessary.)

10. DATE COMPLETED May 10th 76

11. WAS WELL PLUGGED OR ABANDONED?

☐ Yes ☐ No

If so, how

12. REMARKS:

well drilled for park stock.
Estimated potential 10 g.p.m.

13. DRILLER'S CERTIFICATION

This well was drilled under my jurisdiction and this report is true to the best of my knowledge.

Thomas Drlg 29

Driller's or Firm's Name Certificate No.

Cosgrove N.D.

Address

Lloyd R. Thompson

Signed by Date

CATE — BOARD'S COPY
